


ID		Task Mode	Task Name	Text1	Duration	Timeline																											
						Half 2, 2021												Half 1, 2022				Half 1, 2023				Half 2, 2023				Half 1, 2024			
						M	M	J	S	N	J	M	M	J	S	N	J	M	M	J	S	N	J	S	N	J							
1			Centrail Interceptor MTBM		615 days	Centrail Interceptor MTBM																											
2			May Rd A		110 days	May Rd A																											
3			Lifting	120t Crawler Crane	110 days	120t Crawler Crane																											
4			Digger + Attachment	UG Digger + Attachment (14T)	110 days	UG Digger + Attachment (14T)																											
5			Digger	Surface Digger (14T)	110 days	Surface Digger (14T)																											
6			Ventilation	Fan - Zitron gEL9-37/2 (15m3/s)	110 days	Fan - Zitron gEL9-37/2 (15m3/s)																											
7			Ventilation	Gasguard	110 days	Gasguard																											
8			Electrical	Generator Backup (300kVA) + Switchboard	110 days	Generator Backup (300kVA) + Switchboard																											
9			Electrical	2x Sub Pump	110 days	2x Sub Pump																											
10			Container	Container (Tool, rigging, haz)	110 days	Container (Tool, rigging, haz)																											
11			Cage	Cage (4 man, rescue, materials, open)	110 days	Cage (4 man, rescue, materials, open)																											
12			Building	Tally hut + Turnstile	110 days	Tally hut + Turnstile																											
13			Skip	3m3	110 days	3m3																											
14			Grout Pump	Putzmeister S5 EV Grout plant	110 days	Putzmeister S5 EV Grout plant																											
15			Shotcrete	Aliva 272	110 days	Aliva 272																											
16			Compressor	Compressor - 200CFM	110 days	Compressor - 200CFM																											
17			Dundale		60 days	Dundale																											
18			Lifting	120t Crawler Crane	60 days	120t Crawler Crane																											
19			Digger	Digger Telescopic (38T)	60 days	Digger Telescopic (38T)																											
20			Digger + Attachment	UG Digger + Attachment (14T)	60 days	UG Digger + Attachment (14T)																											
21			Digger	Surface Digger (14T)	60 days	Surface Digger (14T)																											
22			Ventilation	Fan - Zitron gEL9-37/2 (15m3/s)	60 days	Fan - Zitron gEL9-37/2 (15m3/s)																											
23			Ventilation	Gasguard	60 days	Gasguard																											
24			Electrical	Generator Backup (250kVA) + Switchboard	60 days	Generator Backup (250kVA) + Switchboard																											
25			Electrical	2x Sub Pump	60 days	2x Sub Pump																											
26			Water Treatment	Water Treatment Plant	60 days	Water Treatment Plant																											
27			Container	Container (Tool, rigging, haz)	60 days	Container (Tool, rigging, haz)																											
28			Cage	Cage (4 man, rescue, materials, open)	60 days	Cage (4 man, rescue, materials, open)																											
29			Skip	3m3	60 days	3m3																											
30			Shotcrete	Aliva 272	60 days	Aliva 272																											
31			Compressor	Compressor - 200CFM	60 days	Compressor - 200CFM																											
32			May Rd B		280 days	May Rd B																											
33			Lifting	160t Crawler Crane	280 days	160t Crawler Crane																											
34			Digger + Attachment	UG Digger + Attachment (23T)	280 days	UG Digger + Attachment (23T)																											
35			Digger + Attachment	UG Digger + Attachment (14T)	185 days	UG Digger + Attachment (14T)																											
36			Digger	Surface Digger (14T)	280 days	Surface Digger (14T)																											
37			Ventilation	Fan - Zitron gEL9-37/2 (15m3/s)	280 days	Fan - Zitron gEL9-37/2 (15m3/s)																											
38			Ventilation	Gasguard	280 days	Gasguard																											
39			Electrical	Generator Backup (300kVA) + Switchboard	280 days	Generator Backup (300kVA) + Switchboard																											
40			Electrical	2x Sub Pump	280 days	2x Sub Pump																											
41			Container	Container (Tool, rigging, haz)	280 days	Container (Tool, rigging, haz)																											
42			Cage	Cage (4 man, rescue, materials, open)	280 days	Cage (4 man, rescue, materials, open)																											
43			Building	Tally hut + Turnstile	280 days	Tally hut + Turnstile																											
44			Skip	4m3	280 days	4m3																											
45			Grout Pump	Putzmeister S5 EV Grout plant	280 days	Putzmeister S5 EV Grout plant																											
46			Shotcrete	Aliva 272	280 days	Aliva 272																											
47			Compressor	Compressor - 200CFM	280 days	Compressor - 200CFM																											
48			Miranda		70 days	Miranda																											
49			Lifting	160t Crawler Crane	70 days	160t Crawler Crane																											
50			Digger	Digger Telescopic (38T)	70 days	Digger Telescopic (38T)																											
51			Digger + Attachment	UG Digger + Attachment (14T)	70 days	UG Digger + Attachment (14T)																											
52			Digger	Surface Digger (14T)	70 days	Surface Digger (14T)																											
53			Ventilation	Fan	70 days	Fan																											
54			Ventilation	Gasguard	70 days	Gasguard																											
55			Electrical	Generator Backup (300kVA) + Switchboard	70 days	Generator Backup (300kVA) + Switchboard																											
56			Electrical	2x Sub Pump	70 days	2x Sub Pump																											
57			Container	Container (Tool, rigging, haz)	70 days	Container (Tool, rigging, haz)																											
58			Cage	Cage (4 man, rescue, materials, open)	70 days	Cage (4 man, rescue, materials, open)																											
59			Building	Tally hut + Turnstile	70 days	Tally hut + Turnstile																											
60			Skip	4m3	70 days	4m3																											
61			Haverstock		175 days	Haverstock																											
62			Lifting	100t Crawler Crane	175 days	100t Crawler Crane																											
63			Digger	Digger Telescopic (38T)	40 days	Digger Telescopic (38T)																											
64			Digger + Attachment	UG Digger + Attachment (8T)	175 days	UG Digger + Attachment (8T)																											
Project: Plant forecasting Date: Thu 8/09/22			<div><div>Task</div><div>Split</div><div>Milestone</div><div>Summary</div><div>Project Summary</div><div>Inactive Task</div><div>Inactive Milestone</div><div>Inactive Summary</div><div>Manual Task</div><div>Duration-only</div><div>Manual Summary Rollup</div><div>Manual Summary</div><div>Start-only</div><div>Finish-only</div><div>External Tasks</div><div>External Milestone</div><div>Deadline</div><div>Progress</div><div>Manual Progress</div></div>																														

Page 1

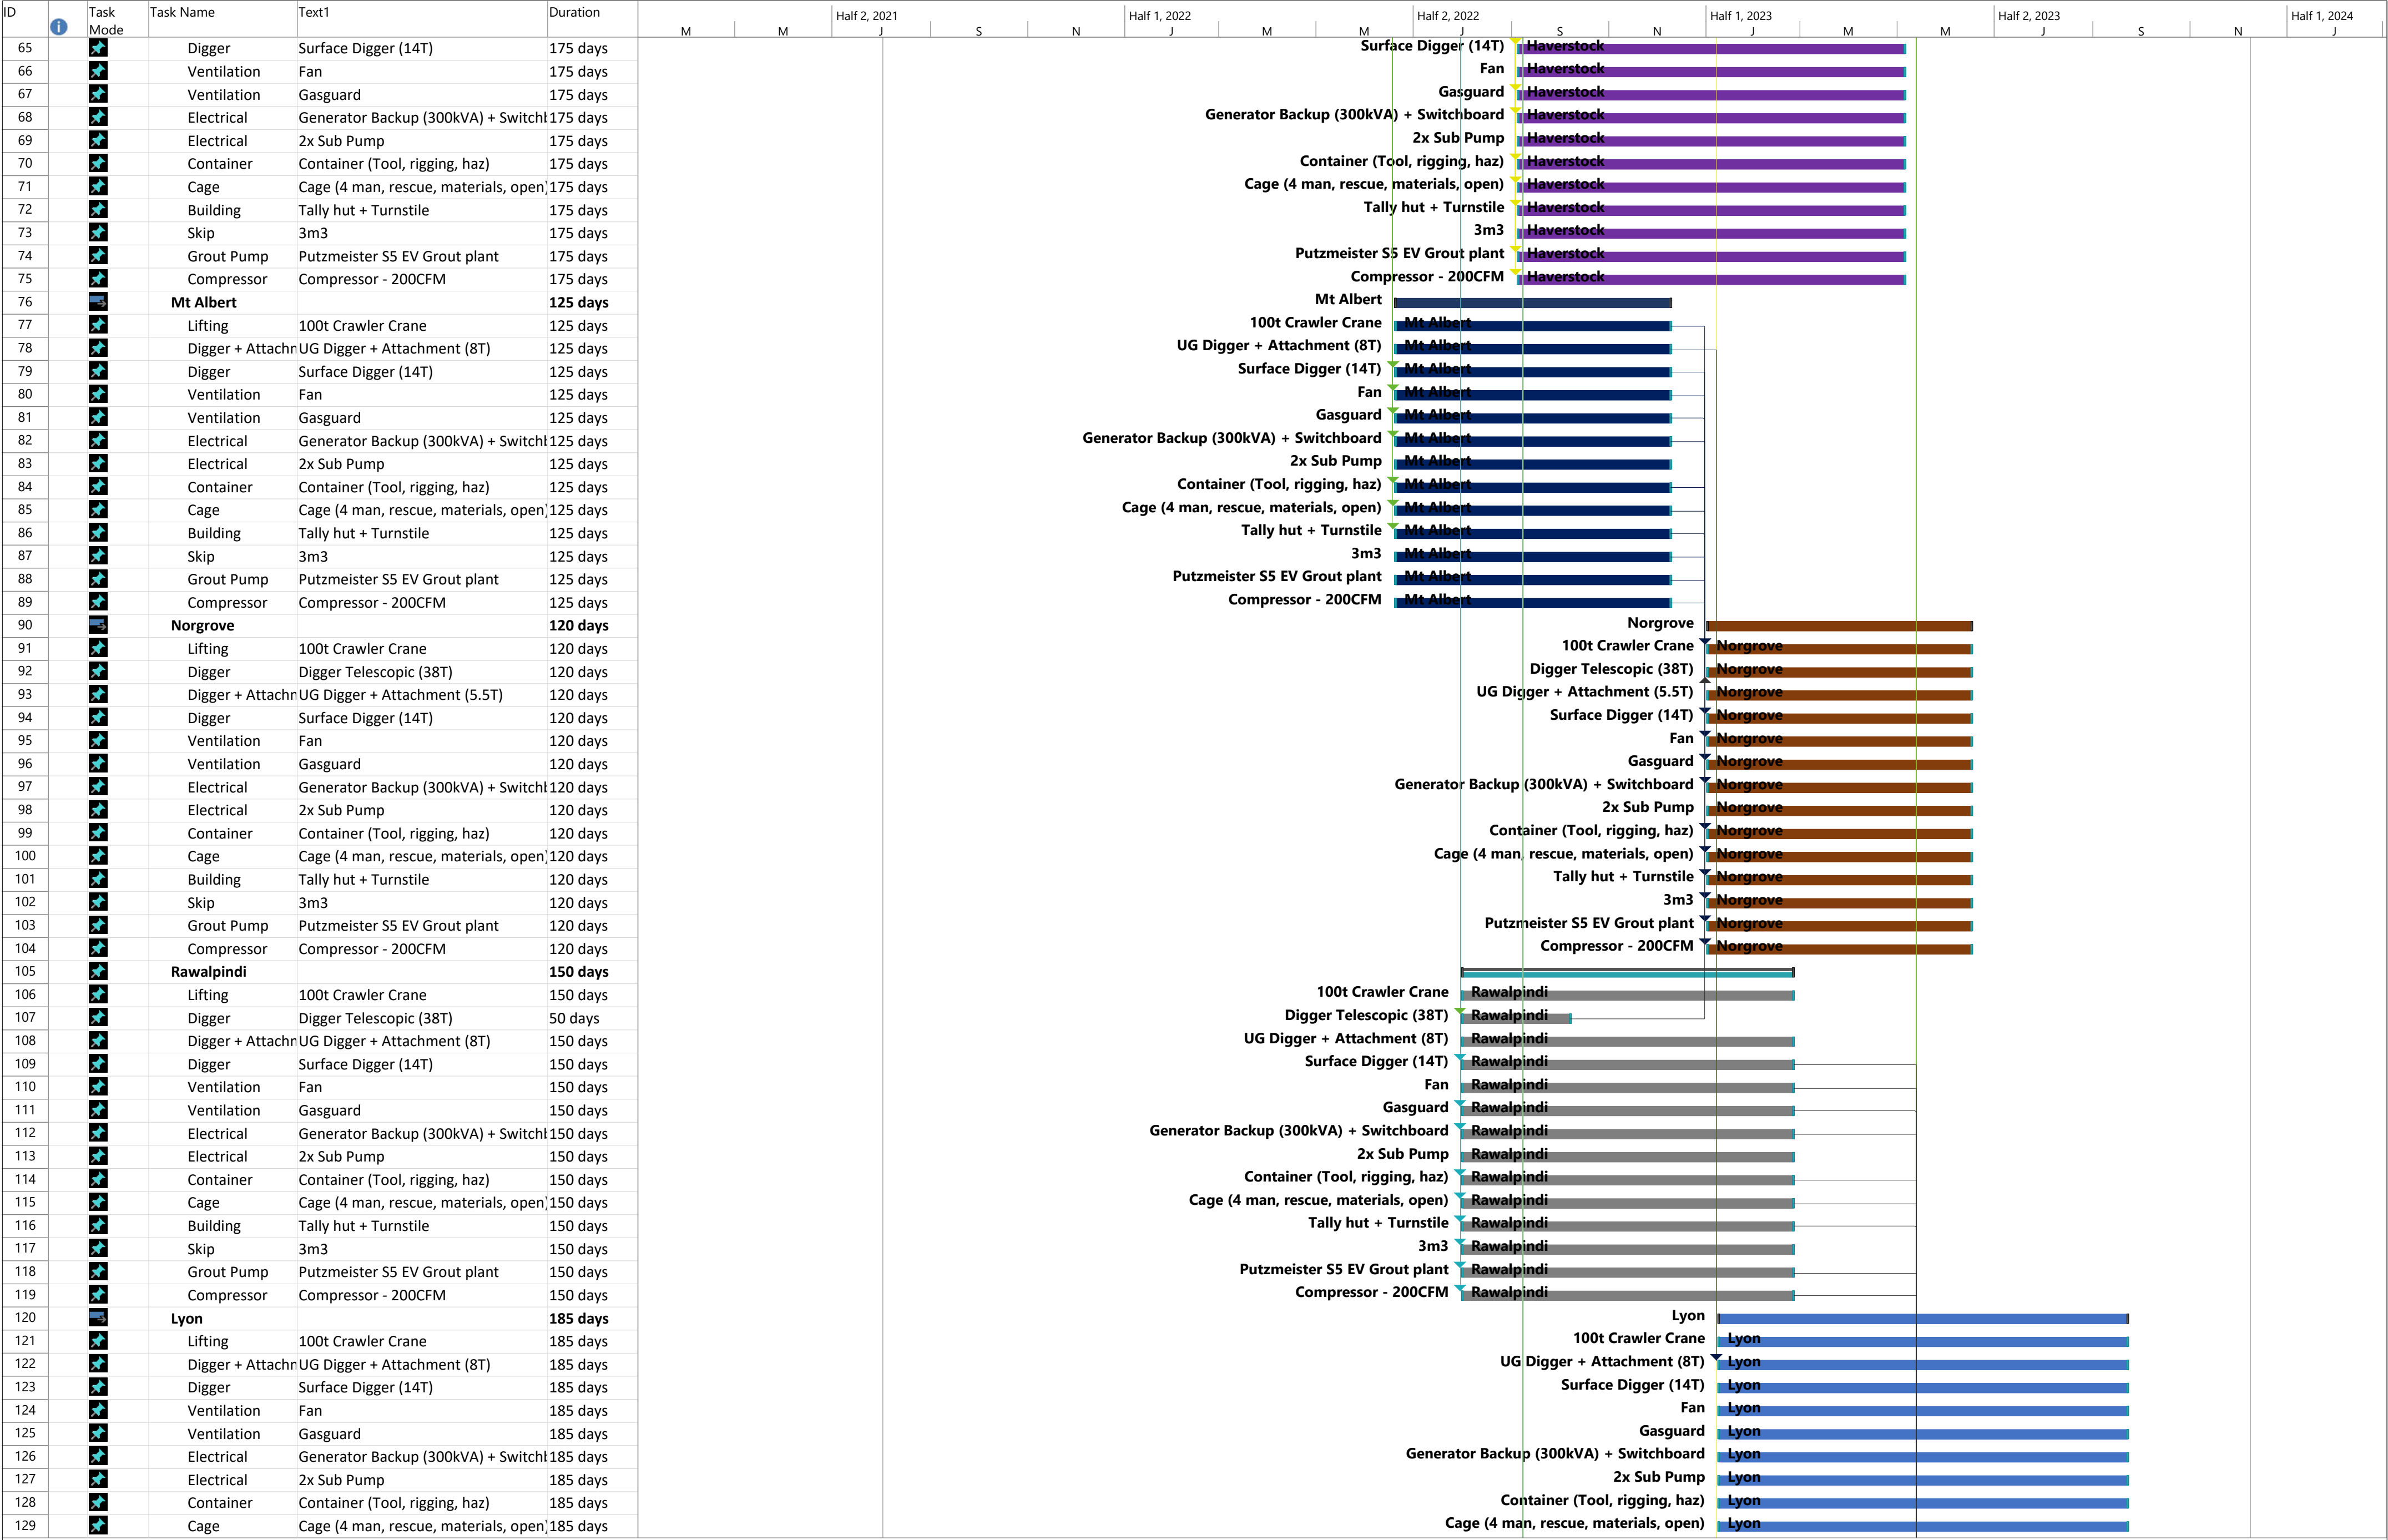

Project: Plant forecasting
Date: Thu 8/09/22

Task	<div></div>	Summary	<div></div>	Inactive Milestone	<div></div>	Duration-only	<div></div>	Start-only	<div></div>	External Milestone	<div></div>	Manual Progress	<div></div>
Split	<div></div>	Project Summary	<div></div>	Inactive Summary	<div></div>	Manual Summary Rollup	<div></div>	Finish-only	<div></div>	Deadline	<div></div>		
Milestone	<div></div>	Inactive Task	<div></div>	Manual Task	<div></div>	Manual Summary	<div></div>	External Tasks	<div></div>	Progress	<div></div>		

